LOCUST STREET PUMP STATION
MAGGIORA & GHILOTTI, INC.

ID	Task Name	Duration	Start	Finish	Predecessors
1	NOTICE TO PROCEED	1 day	Thu 7/14/11	Thu 7/14/11	
2	PRE-CONSTRUCTION MEETING	1 day	Fri 7/15/11	Fri 7/15/11	1
3	SUBMITTALS	20 days	Mon 7/18/11	Fri 8/12/11	2
4	SIGNS, NOTIFICATIONS	1 day	Mon 8/15/11	Mon 8/15/11	3
5	SURVEY, LAYOUT & CONTROL	4 days	Tue 8/16/11	Fri 8/19/11	4
6	TEMP SWPPP CONTROL	1 day	Mon 8/22/11	Mon 8/22/11	5
7	MOBILIZATION	2 days	Tue 8/23/11	Wed 8/24/11	6
8	K RAIL - PEDESTRIAN ACCESS	2 days	Thu 8/25/11	Fri 8/26/11	7
9	POTHOLING	5 days	Mon 10/3/11	Fri 10/7/11	8
10	TEMPORARY POWER-INCLUDING POLE	5 days	Mon 11/7/11	Fri 11/11/11	9
11	RELOCATE WATER MAIN, SERVICES, FIRE HYDRANT	5 days	Mon 10/17/11	Fri 10/21/11	9
12	TRENCH FOR PG&E GAS MAIN	10 days	Mon 10/31/11	Fri 11/11/11	10FF,11
13	TRENCH AND CONDUIT FOR ATT/ELECTRIC	5 days	Mon 11/14/11	Fri 11/18/11	12
14	PHASE I BYPASS SYSTEM	3 days	Mon 11/21/11	Wed 11/23/11	
15	PHASE II BYPASS SYSTEM	3 days	Mon 5/9/11	Wed 5/11/11	
16	PHASE III BYPASS SYSTEM	10 days	Thu 5/12/11	Wed 5/25/11	15
17	DEMO MH - CONSTRUCT NEW	5 days	Mon 12/5/11	Fri 12/9/11	16FF
18	NEW 4', 5' AND 6' DIA MH'S	5 days	Mon 12/12/11	Fri 12/16/11	17
19	FLOW METER VAULT	5 days	Mon 12/19/11	Fri 12/23/11	17
20	INSTALL 10' DIAMETER RCP	10 days	Mon 1/16/12	Fri 1/27/12	19SS
21	POUR BOTTOM SLAB, DOWELS, FILLET	5 days	Mon 1/23/12	Fri 1/27/12	20FF
22	INSTALL RCP CONNECTORS	5 days	Mon 1/23/12	Fri 1/27/12	20FF
23	EXCAVATE VALVE PIT	2 days	Thu 1/26/12	Fri 1/27/12	22FF
24	FORM, POUR, STRIP, WATERPROOF VALVE PIT	5 days	Mon 1/30/12	Fri 2/3/12	23
25	DECK AND HATCHES	5 days	Mon 2/6/12	Fri 2/10/12	24
26	INSTALL PUMPS	5 days	Mon 2/13/12	Fri 2/17/12	25
27	HELICAL ANCHOR SUB	5 days	Mon 2/6/12	Fri 2/10/12	25FF
28	FORM, POUR MCC PAD	5 days	Mon 2/6/12	Fri 2/10/12	27FF
29	MASONRY WALL	5 days	Mon 2/13/12	Fri 2/17/12	28
30	METAL SEAM ROOF	2 days	Thu 2/16/12	Fri 2/17/12	29FF
31	FENCE	2 days	Thu 2/16/12	Fri 2/17/12	29FF
32	SET REFURBISHED GENERATOR	5 days	Mon 2/20/12	Fri 2/24/12	31
33	DEMO INTERIOR/EXTERIOR PUMP STATION	5 days	Mon 2/20/12	Fri 2/24/12	
34	FORM, POUR SIDEWALK, CURB & GUTTER	5 days	Mon 2/20/12	Fri 2/24/12	33FF
35	PAINTING AND COATING	3 days	Wed 2/22/12	Fri 2/24/12	32FF
36	REMOVE GENERATOR - HOOK UP STAND BY	5 days	Mon 2/27/12	Fri 3/2/12	35
37	ELECTRICAL(MCC ON-SITE)	5 days	Mon 2/27/12	Fri 3/2/12	35
38	WIRE MCC, TEST AND START UP	15 days	Mon 3/5/12	Fri 3/23/12	37,33FF,34FF
39	AC PAVING AND STRIPING	5 days	Mon 3/19/12	Fri 3/23/12	38FF
40	CLEAN UP AND PUNCH LIST	3 days	Mon 3/26/12	Wed 3/28/12	39
41	DEMOBILIZATION	2 days	Thu 3/29/12	Fri 3/30/12	40

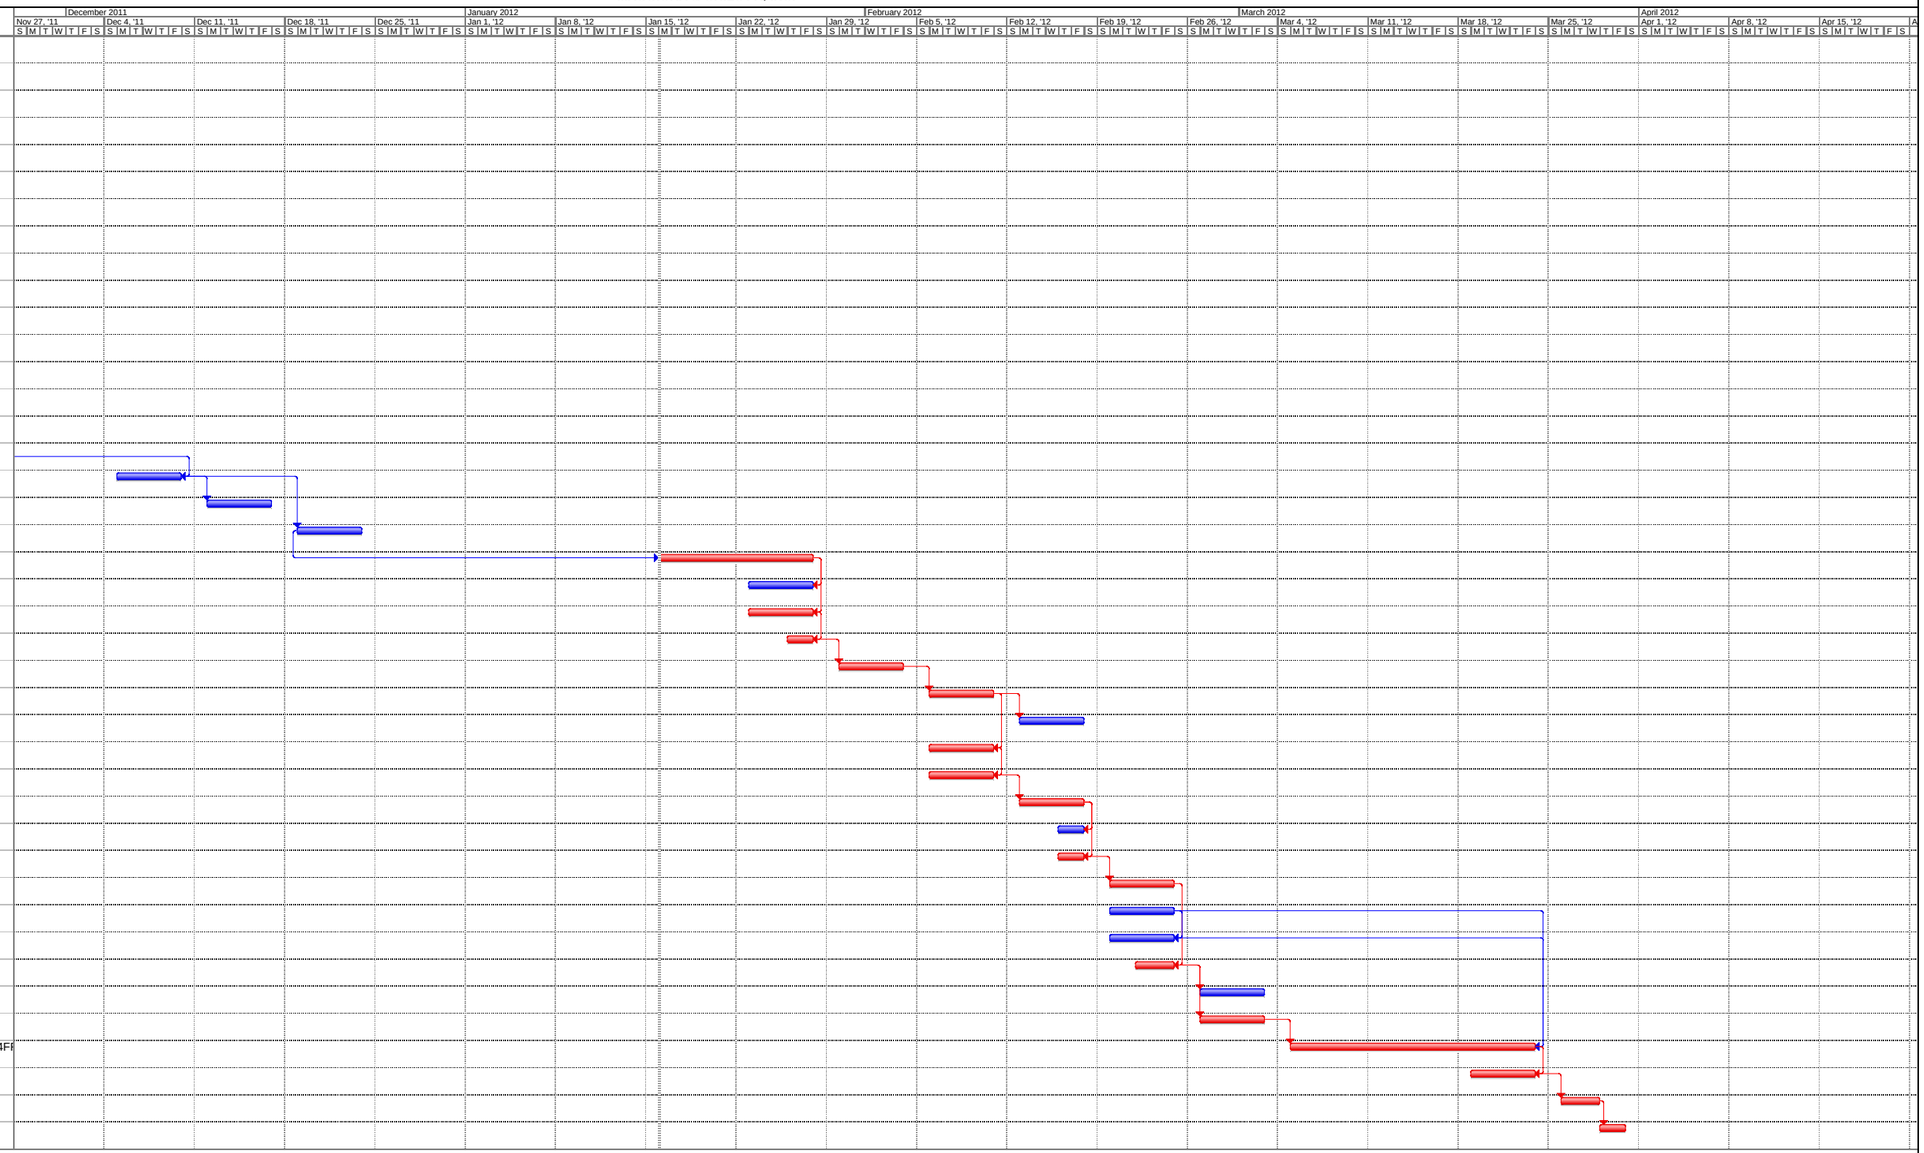

Project: LOCUST STREET PUMP STATION-1-16-12.mpp
Date: Mon 1/16/12

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary | Deadline
