Lycee - Marin Campus

ID	Task Name	Duration	Start	Finish
1	**General Business**	**41 days**	**Fri 2/8/13**	**Fri 3/29/13**
2	Mobilize to Cap at Plan Check Comments	0 days	Fri 2/8/13	Fri 2/8/13
3	Issue Final Bid Documents	1 day	Fri 3/8/13	Fri 3/8/13
4	City's Re-review period	15 days	Fri 3/8/13	Thu 3/28/13
5	Full scaffolding & Demolition Permit	5 days	Fri 2/22/13	Thu 2/28/13
6	All bids Due	0 days	Fri 2/15/13	Fri 2/15/13
7	Approve Budget	0 days	Fri 3/29/13	Fri 3/29/13
8	Notice to Proceed	1 day	Fri 3/29/13	Fri 3/29/13
9	Write subcontracts	5 days	Mon 4/1/13	Fri 4/5/13
10	Submittals	20 days	Mon 4/8/13	Fri 5/3/13
11	Confirm Pre-K Licensing Agreement	0 days	Fri 3/15/13	Fri 3/15/13
12	Confirm site AQM issues	0 days	Fri 3/15/13	Fri 3/15/13
13	Marin School - Last Day of Classes	1 day	Fri 3/29/13	Fri 3/29/13
14	Marin School Moves Out	10 days	Mon 4/1/13	Fri 4/12/13
15	Webcor complete inventory	10 days	Mon 4/1/13	Fri 4/12/13
16	site Hardestabilization	5 days	Fri 4/5/13	Thu 4/11/13
17	Set Salvage Containers	1 day	Mon 4/1/13	Mon 4/1/13
18	Salvage Inventory from Corte Madera	20 days	Mon 4/1/13	Fri 4/26/13
19				
20	**General Construction**	**58 days**	**Mon 4/1/13**	**Wed 7/31/13**
21	Day one	0 days	Mon 4/1/13	Mon 4/1/13
22	Electrical Safe-Off	5 days	Mon 4/1/13	Fri 4/5/13
23	Plumbing Safe Off	5 days	Mon 4/1/13	Fri 4/5/13
24	Owner Salvage	5 days	Mon 4/1/13	Fri 4/5/13
25	Identify Demolition Scope	5 days	Mon 4/1/13	Fri 4/5/13
26				
27	**Building 3**	**55 days**	**Mon 4/22/13**	**Fri 7/5/13**
28	Interior Soft Demolition	5 days	Mon 4/22/13	Fri 4/26/13
29	Rebuild Shear Walls	5 days	Mon 4/29/13	Fri 5/3/13
30	HM+Frame door openings and Headers	5 days	Mon 4/29/13	Fri 5/3/13
31	Overhead Electrical & Fire Ro-In	10 days	Mon 5/6/13	Fri 5/17/13
32	Overhead Fire Modifications	5 days	Mon 5/6/13	Fri 5/10/13
33	Overhead Mechanical Re-work	5 days	Mon 5/6/13	Fri 5/10/13
34	Electrical Ro-In Walls	5 days	Mon 5/6/13	Fri 5/10/13
35	Sheetrock Walls	3 days	Mon 5/13/13	Wed 5/15/13
36	Taps, Top and Finish walls	10 days	Thu 5/16/13	Wed 5/29/13
37	Insulate Ceilings	2 days	Thu 5/30/13	Fri 5/17/13
38	Paint Walls	5 days	Thu 5/30/13	Wed 6/5/13
39	Re-Install Spline Ceilings	5 days	Thu 6/6/13	Wed 6/12/13
40	Hemitlate Light+Outlets	5 days	Thu 6/13/13	Wed 6/19/13
41	Fire & life Safety	10 days	Thu 6/13/13	Wed 6/26/13
42	Set Casework	2 days	Thu 6/20/13	Fri 6/21/13
43	Install door Frames	2 days	Thu 6/6/13	Mon 6/10/13
44	Install Finish Flooring	5 days	Mon 6/24/13	Fri 6/28/13
45	Swing Doors & Install Hardware	3 days	Mon 7/1/13	Wed 7/3/13
46	Trim Out Phone & Data	10 days	Thu 6/6/13	Wed 6/19/13
47	Epoxy Floor & Walls in restrooms	5 days	Thu 6/6/13	Wed 6/12/13
48	Install Plumbing Trim	5 days	Mon 6/24/13	Fri 6/28/13
49	Toilet Room Partitions	5 days	Mon 7/1/13	Fri 7/5/13
50				
51	**Building 4**	**50 days**	**Mon 4/22/13**	**Fri 6/28/13**
52	Interior Soft Demolition	10 days	Mon 4/22/13	Fri 5/3/13
53	Rebuild Shear Walls	5 days	Mon 5/6/13	Fri 5/10/13
54	HM+Frame door openings and Headers	5 days	Mon 5/6/13	Fri 5/10/13
55	Overhead Electrical & Fire Ro-In	10 days	Mon 5/13/13	Fri 5/24/13
56	Overhead Fire Modifications	5 days	Mon 5/13/13	Fri 5/17/13
57	Overhead Mechanical Re-work	5 days	Mon 5/13/13	Fri 5/17/13
58	Electrical Ro-In Walls	5 days	Mon 5/13/13	Fri 5/17/13
59	Sheetrock Walls	3 days	Mon 5/20/13	Wed 5/22/13
60	Taps, Top and Finish walls	10 days	Thu 5/23/13	Wed 6/5/13
61	Insulate Ceilings	2 days	Thu 6/6/13	Fri 6/7/13
62	Paint Walls	5 days	Thu 6/6/13	Wed 6/12/13
63	Re-Install Spline Ceilings	5 days	Thu 6/13/13	Wed 6/19/13
64	Hemitlate Light+Outlets	5 days	Thu 6/20/13	Wed 6/26/13
65	Fire & life Safety	10 days	Thu 6/13/13	Wed 6/26/13
66	Set Casework	2 days	Thu 6/13/13	Fri 6/14/13
67	Install door Frames	2 days	Thu 6/13/13	Mon 6/17/13
68	Install Finish Flooring	5 days	Mon 6/17/13	Fri 6/21/13
69	Swing Doors & Install Hardware	3 days	Mon 6/24/13	Wed 6/26/13
70	Trim Out Phone & Data	10 days	Thu 6/13/13	Wed 6/26/13
71	Epoxy Floor & Walls in restrooms	5 days	Thu 6/13/13	Wed 6/19/13
72	Install Plumbing Trim	5 days	Mon 6/17/13	Fri 6/21/13
73	Toilet Room Partitions	5 days	Mon 6/24/13	Fri 6/28/13
74				
75	**Building 5**	**73 days**	**Mon 4/22/13**	**Wed 7/31/13**
76	Interior Soft Demolition	10 days	Mon 4/22/13	Fri 5/3/13
77	Rebuild Shear Walls	5 days	Mon 5/13/13	Fri 5/17/13
78	HM+Frame door openings and Headers	5 days	Mon 5/13/13	Fri 5/17/13
79	Overhead Electrical & Fire Ro-In	10 days	Mon 5/20/13	Fri 5/31/13
80	Overhead Fire Modifications	5 days	Mon 5/20/13	Fri 5/24/13
81	Overhead Mechanical Re-work	5 days	Mon 5/20/13	Fri 5/24/13
82	Electrical Ro-In Walls	5 days	Mon 5/20/13	Fri 5/24/13
83	Sheetrock Walls	3 days	Mon 5/27/13	Wed 5/29/13
84	Taps, Top and Finish walls	10 days	Thu 5/30/13	Wed 6/12/13
85	Insulate Ceilings	2 days	Thu 6/13/13	Fri 6/14/13
86	Paint Walls	5 days	Thu 6/13/13	Wed 6/19/13
87	Insulate Open Ceiling Area	5 days	Thu 6/20/13	Wed 6/26/13
88	Install Acoustical Panel Ceilings at Upper Areas	2 days	Thu 6/27/13	Mon 7/1/13
89	Recessed Light Fixtures	5 days	Tue 7/2/13	Mon 7/8/13
90	Fire & life Safety	10 days	Thu 6/20/13	Wed 7/3/13
91	Set Casework	2 days	Thu 6/20/13	Fri 6/21/13
92	Install door Frames	2 days	Thu 6/20/13	Mon 6/24/13
93	Install Finish Flooring	5 days	Mon 6/24/13	Fri 6/28/13
94	Swing Doors & Install Hardware	3 days	Mon 7/1/13	Wed 7/3/13
95	Trim Out Phone & data	10 days	Thu 6/20/13	Wed 7/3/13
96	Epoxy floor & Walls in Restrooms	5 days	Thu 6/20/13	Wed 6/26/13
97	Finish Ceramic Tile Floors in Restrooms	5 days	Thu 6/27/13	Wed 7/3/13
98	Install Plumbing Trim	5 days	Thu 7/4/13	Wed 7/10/13
99	Toilet Room Partitions	5 days	Thu 7/11/13	Wed 7/17/13
100	TCO	0 days	Wed 7/17/13	Wed 7/17/13
101	Unlocker Licensing	10 days	Thu 7/18/13	Wed 7/31/13
102				
103	**Site Schedule**	**68 days**	**Mon 4/15/13**	**Wed 7/17/13**
104	Layout new Islands	5 days	Mon 4/15/13	Fri 4/19/13
105	Hire Hardscape	5 days	Mon 4/22/13	Fri 5/3/13
106	AC Cut and remove	2 days	Mon 5/6/13	Wed 5/1/13
107	Re-Grade for new walls	5 days	Thu 5/2/13	Wed 5/8/13
108	Remove Rock and re-Grade for new sidewalks	5 days	Thu 5/2/13	Wed 5/8/13
109	Form and pour new sidewalks	5 days	Thu 5/9/13	Wed 5/15/13
110	Form and Pour New Curbs	5 days	Thu 5/2/13	Wed 5/8/13
111	Irrigation to new planters	3 days	Thu 5/2/13	Mon 5/6/13
112	Master planters	2 days	Thu 5/9/13	Fri 5/10/13
113	Planting & Irrigation	5 days	Mon 5/13/13	Fri 5/17/13
114	Pre-K Retaining Walls	15 days	Thu 5/9/13	Wed 5/29/13
115	Form and Pour New Pre-K Sidewalks	5 days	Thu 5/30/13	Wed 6/5/13
116	Underground Storm Drains	5 days	Thu 5/30/13	Wed 6/5/13
117	Backfill Walls and Grade Pre-K	5 days	Thu 6/6/13	Wed 6/12/13
118	Install Fence at Pre-K	5 days	Thu 6/13/13	Wed 6/19/13
119	Install site Furnitur and cabin	10 days	Thu 6/20/13	Wed 7/3/13
120	Patch AC and Level HDCP trails	5 days	Thu 7/4/13	Wed 7/10/13
121	Re-Stripe & Signs	2 days	Thu 7/11/13	Fri 7/12/13
122	Install Play structure at Pre-K	5 days	Thu 6/13/13	Wed 6/19/13
123	Install Tribe Path at Pre-K	10 days	Thu 6/20/13	Wed 7/3/13
124	Landscaping and Irrigation at Pre-K	5 days	Thu 7/4/13	Wed 7/10/13
125	Sand and Bark Areas at Pre-K	5 days	Thu 7/11/13	Wed 7/17/13
126				
127	**Exterior Lead Paint and Re-Paint Schedule**	**73 days**	**Mon 4/1/13**	**Wed 7/10/13**
128	Chip and Prep Building 5 & Canopy	20 days	Mon 4/1/13	Fri 4/26/13
129	Chip and Prep sandblaj 4 & Canopy	20 days	Mon 4/1/13	Fri 5/24/13
130	Chip and Prep sandblaj 2 & Canopy	20 days	Mon 5/27/13	Fri 6/21/13
131	Paint Building 5	5 days	Thu 7/4/13	Wed 7/10/13
132	Paint Building 4	5 days	Tue 6/18/13	Mon 6/24/13
133	Paint sandblaj 2	5 days	Tue 6/11/13	Mon 6/17/13

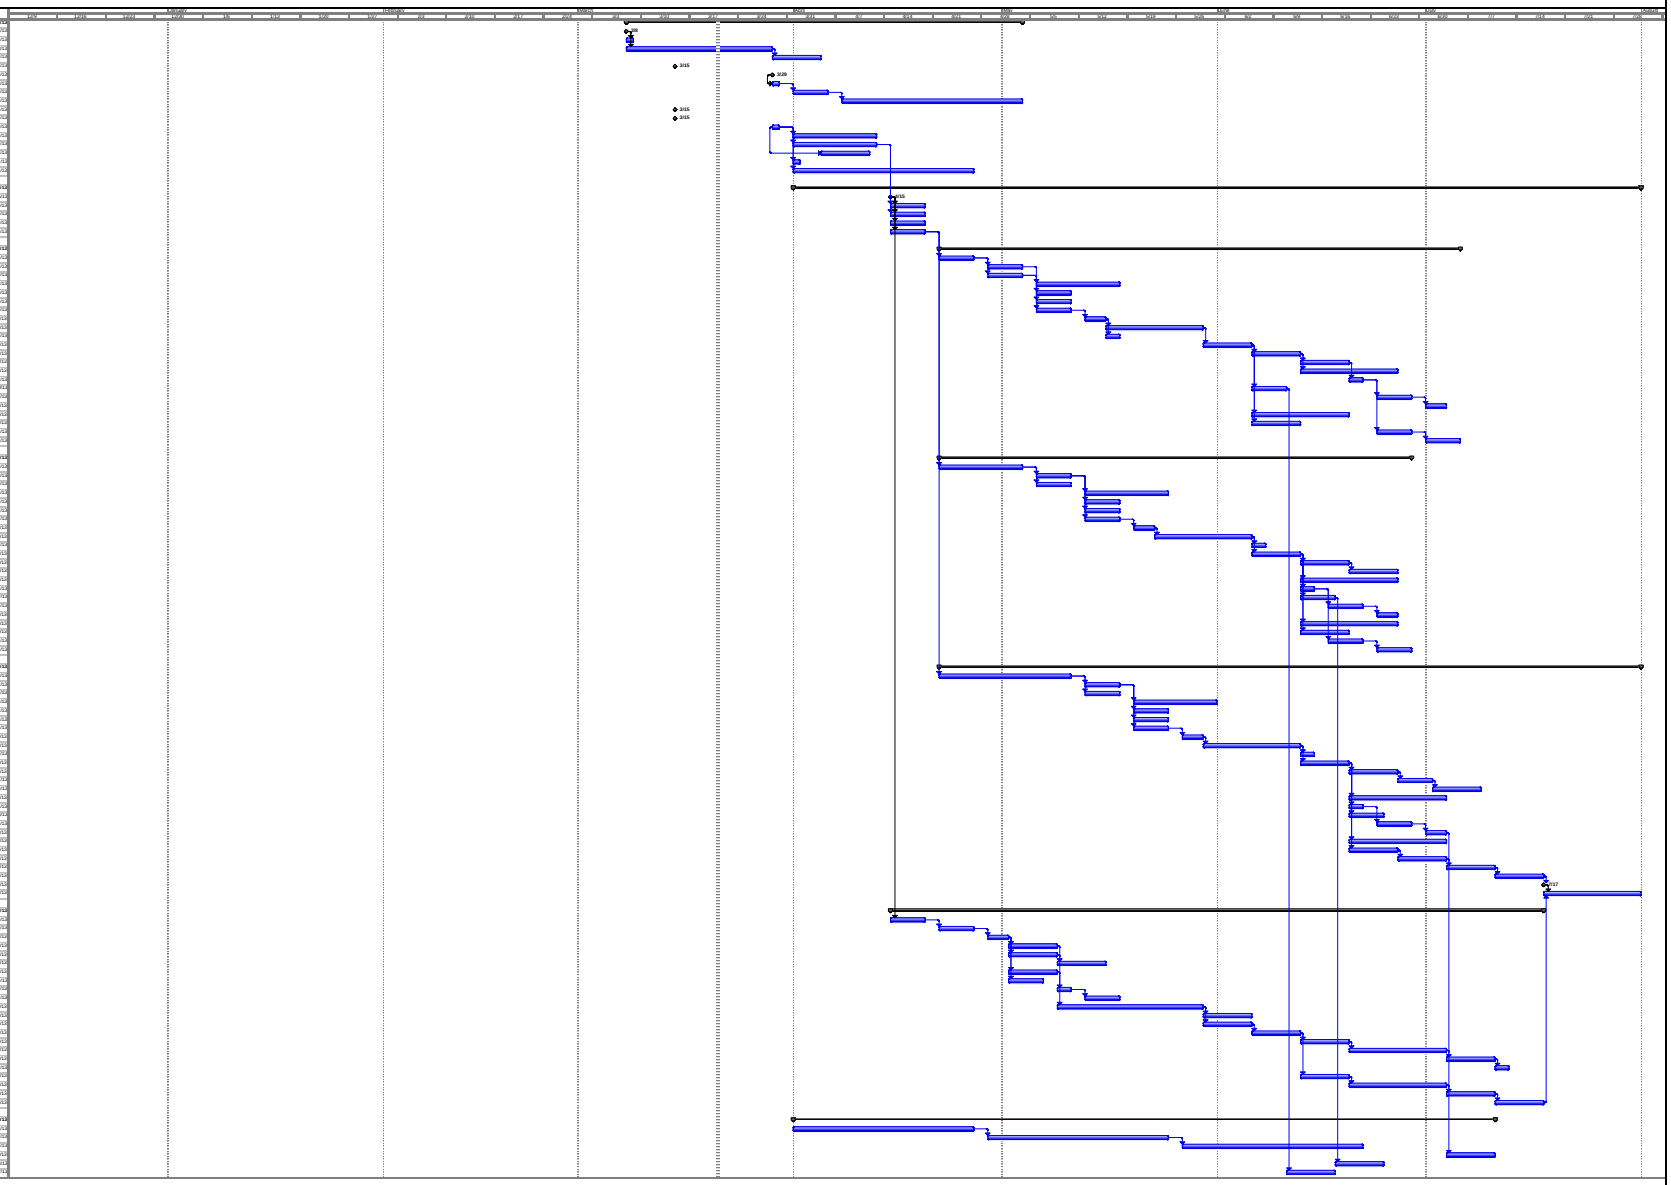

Project: Bid Schedule 2-5-13
Date: Thu 3/21/13

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
